

PROJECT BASELINE COMPARISON REPORT

STATUS DATE: Wed 7/27/11

BEAUMONT_INDEPENDENT_SCHOOL_DISTRICT




Project: BEAUMONT_INDEPENDENT_SCHOOL_DIS
 Project Status Date: Fri 7/15/11
 Report Date: Wed 7/27/11

Current Plan Baseline Plan Baseline Milestone Baseline Summary Baseline Proj Sum Su Current Plan
 Current Plan Critical Milestone Summary Project Summary Task Progress

PROJECT BASELINE COMPARISON REPORT

STATUS DATE: Wed 7/27/11

BEAUMONT_INDEPENDENT_SCHOOL_DISTRICT

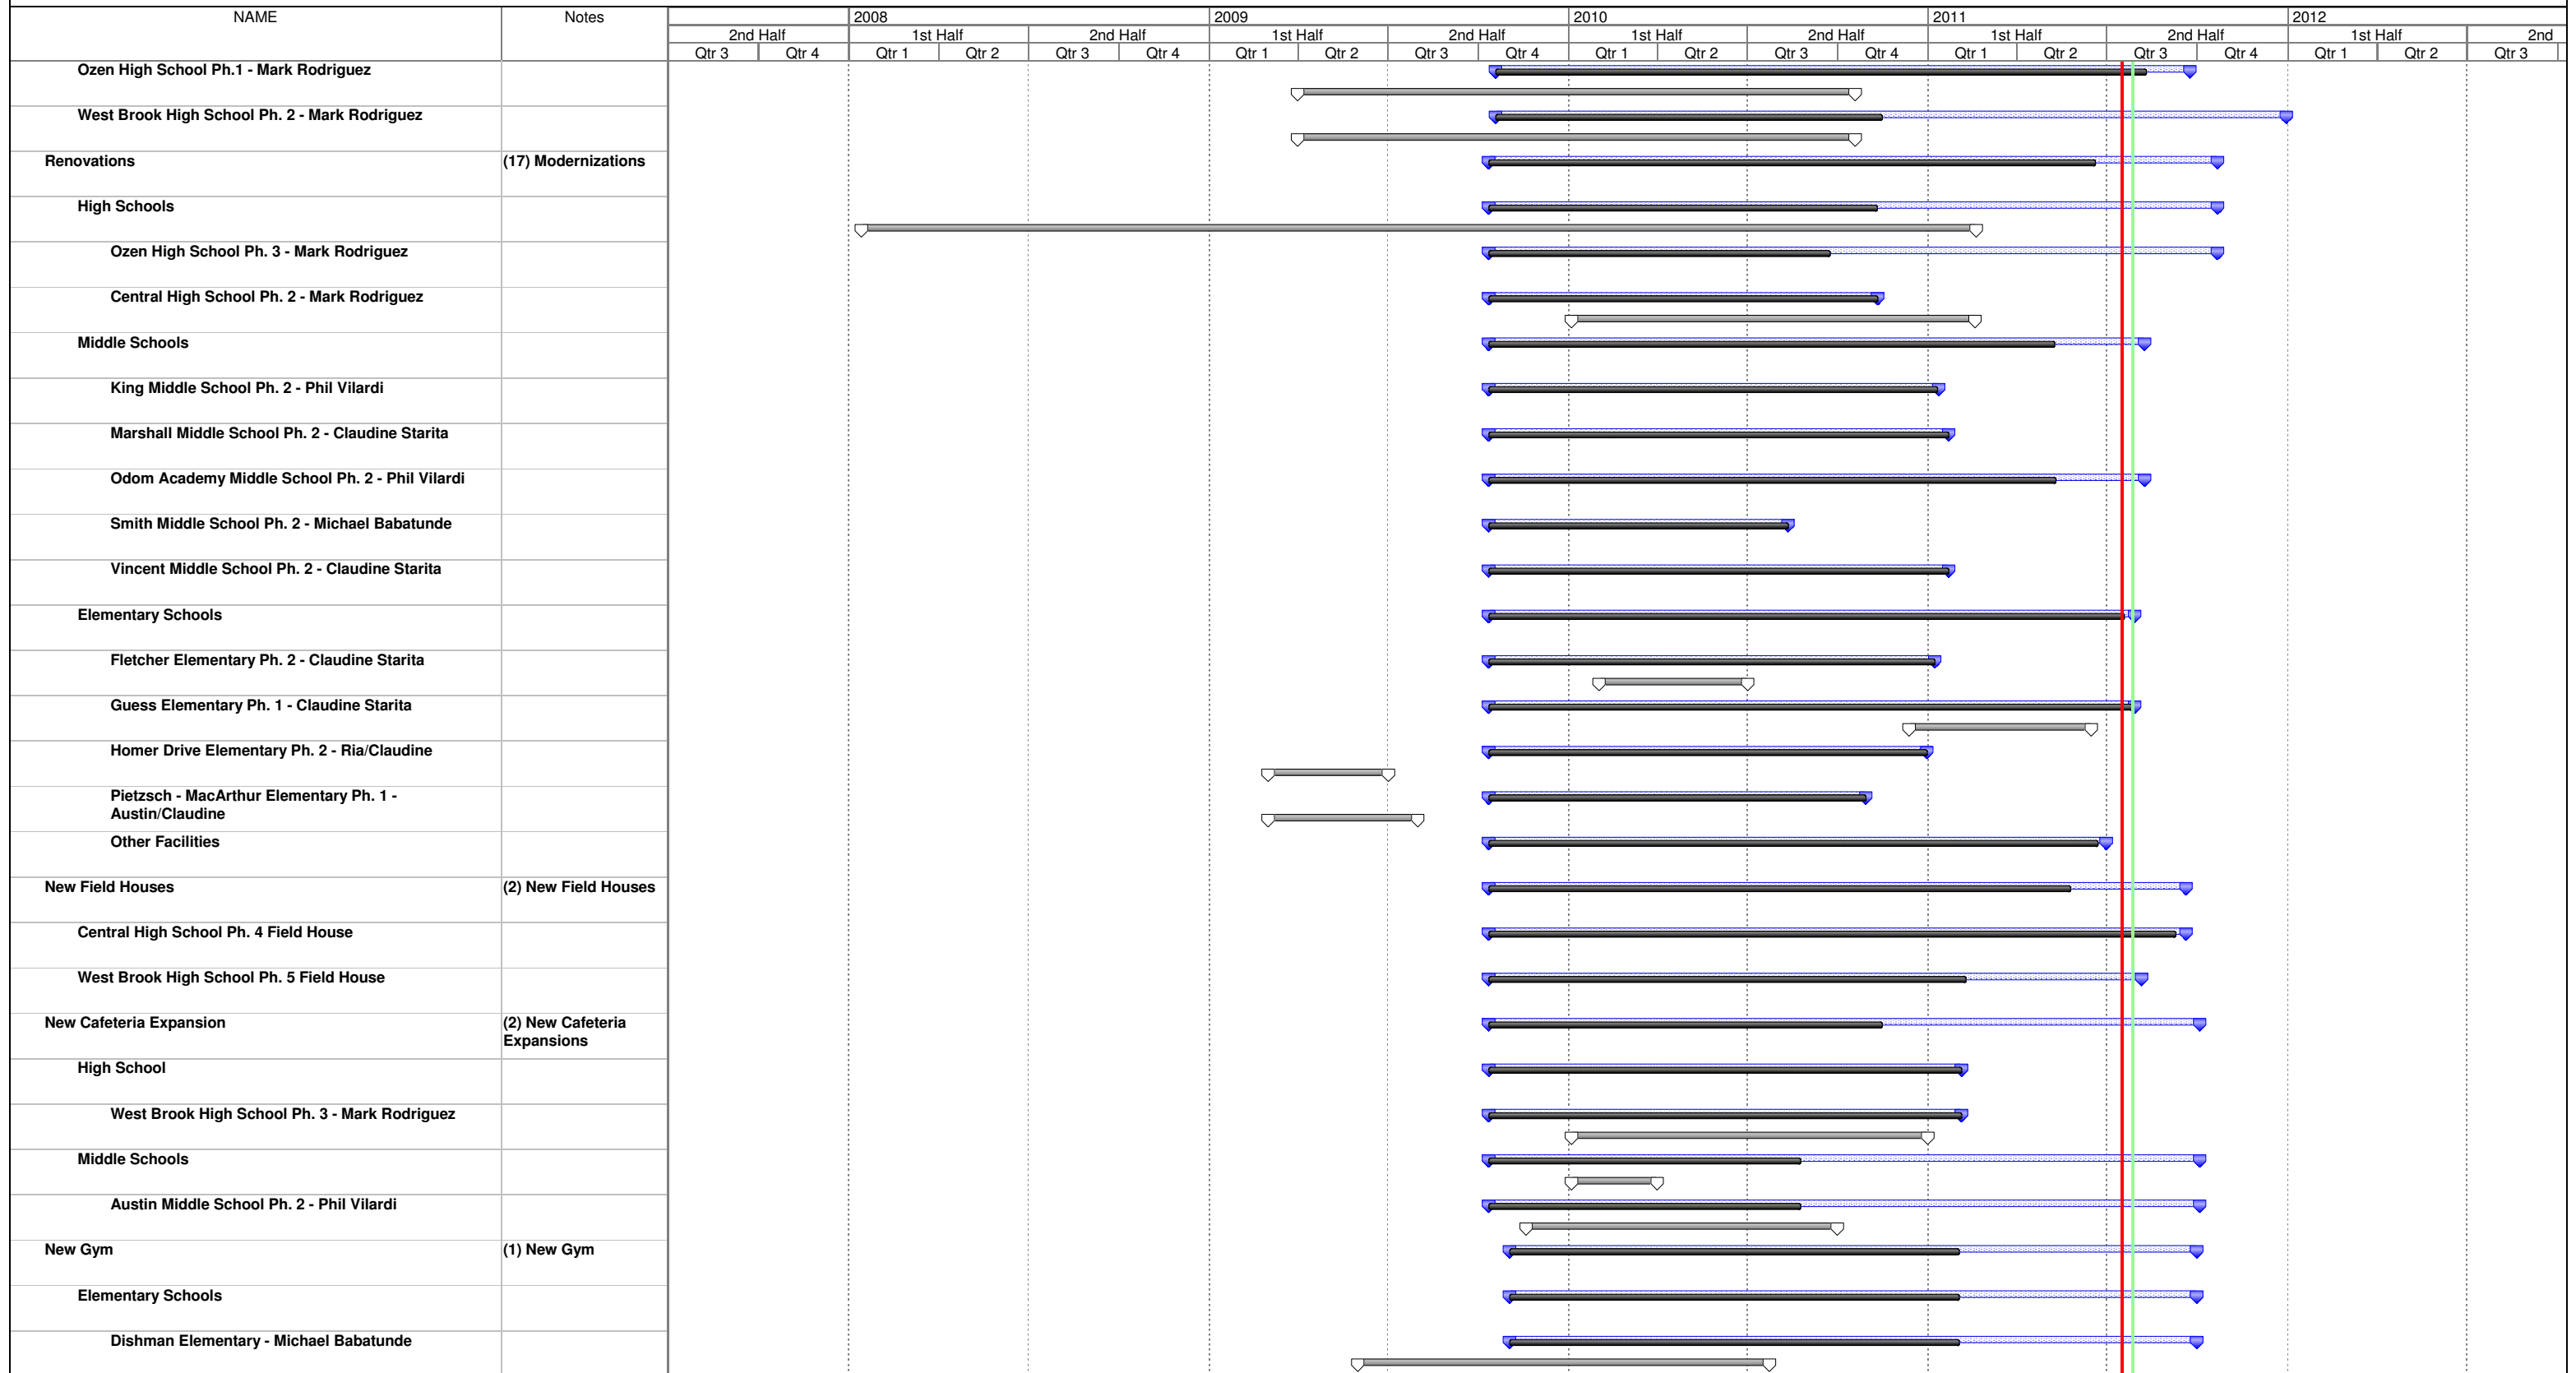

Project: BEAUMONT_INDEPENDENT_SCHOOL_DIS
 Project Status Date: Fri 7/15/11
 Report Date: Wed 7/27/11

Current Plan Baseline Plan Baseline Milestone Baseline Summary Baseline Proj Sum Su Current Plan
 Current Plan Critical Milestone Summary Project Summary Task Progress











PROJECT BASELINE COMPARISON REPORT

STATUS DATE: Wed 7/27/11

BEAUMONT_INDEPENDENT_SCHOOL_DISTRICT

NAME	Notes	2008		2009		2010		2011		2012														
		1st Half		1st Half		1st Half		1st Half		1st Half														
		Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2											
Roof Upgrades	(9) Roof Upgrades																							
High Schools																								
Central High School Ph.3 - Bob Menefee																								
West Brook High School Ph.4 - Bob Menefee																								
Middle Schools																								
Odom Academy Middle School Ph.3 - Bob Menefee																								
Elementary Schools																								
Bingman Elementary Ph. 2 - Bob Menefee																								
Fletcher Elementary Ph. 3 - Bob Menefee																								
Lucas Elementary Ph. 2 - Bob Menefee																								
Pietzsh-MacArthur Elementary Ph. 2 - Bob Menefee																								
Other Facilities																								
Brown-Alternative Ph. 2 - Bob Menefee																								
Transportation - Bob Menefee																								
Special Projects																								

Project: BEAUMONT_INDEPENDENT_SCHOOL_DIS
 Project Status Date: Fri 7/15/11
 Report Date: Wed 7/27/11

Current Plan  Baseline Plan  Baseline Milestone  Baseline Summary  Baseline Proj Sum  Su Current Plan 
 Current Plan Critical  Milestone  Summary  Project Summary  Task Progress 
